
1 · GW additions by state in Aterio's census — 2026-30, by stage and likelihood

ATERIO

Aterio has 352 GW with an activation date in 2026-30 in the US; 208 GW (59%) is high likelihood. Only 71.5 GW (20%) is under construction — the rest is announced. Texas alone has 97 GW (27%); the top five states, 55%.

GW with an activation date in 2026-30, by state

14 largest states + 30 others · facility GW · announced split by Aterio's likelihood

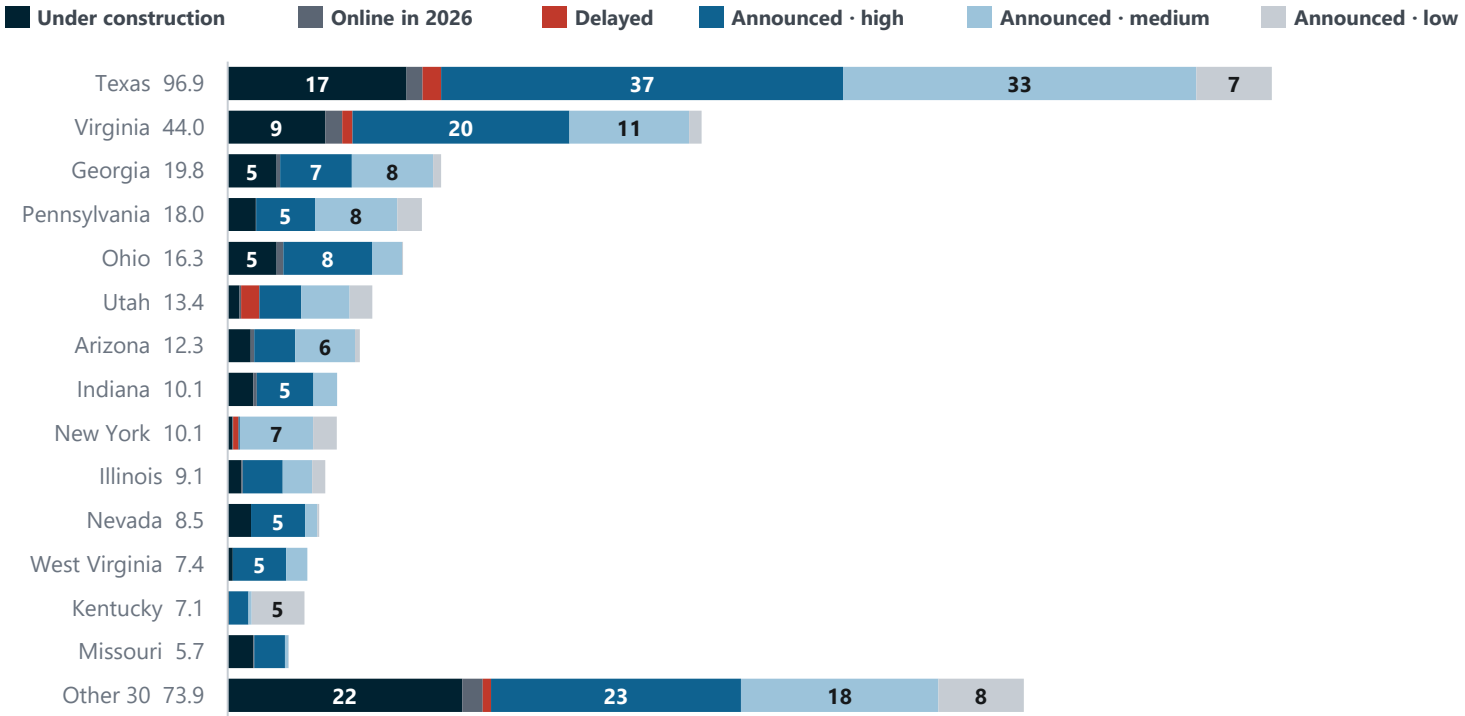

ADDITIONS 2026-30

352 GW

facility · stated activation date

HIGH LIKELIHOOD

208 GW

59% of total · construction is ~99% high

UNDER CONSTRUCTION

71.5 GW

20% · medium + low: 136 GW

TEXAS

97 GW

57% high · 16.6 GW building

By activation year

facility GW, US

Year	Adds	Building	Announced	% announced
2026	20.2	13.1	0.0	0%
2027	43.5	27.0	15.5	36%
2028	116.1	26.8	87.7	76%
2029	103.6	3.5	97.6	94%
2030	68.9	1.1	67.3	98%
2026-30	**352.5**	**71.5**	**268.3**	**76%**

Reading: Aterio's curve is everything with a date, not a forecast. 2026-27 (63.7 GW) is 76% under construction or already online; 2028 (116 GW) and 2029 (104 GW) are 76% and 94% announced. Medium + low likelihood adds up to 136 GW — that is where the slide-3 scenarios cut.

Source: Aterio data-center census (inventory as of 31-Aug-26; weekly report with the 27-Aug-26 forecast) — licensed, internal use; Capstone calculations. **GW = facility power** (SELECTED_POWER_CAPACITY_MW), building level — not IT load (facility/IT ~1.15 in the same data) nor the campus-level cut of the reference deck (139.5 GW). Additions = live buildings (excl. cancelled/withdrawn) with an activation date in 2026-30; 'online in 2026' = active buildings activated in 2026. Likelihood is set per campus by Aterio; its definition (GS-hosted call, 20-Oct-26): high >80% materialise, medium ~50-60%, low <40%.


2 · Delay: what Aterio already flags — delayed stage, dates and track record

ATERIO

Aterio publishes no 'GW delayed' number; delay shows up in three places: 8.8 GW flagged as delayed, its own dates a median 14 months after the public source on 43% of comparable MW, and a track record where 88% of what was under construction a year ago had its date pushed out (median 9 months).

① 'Delayed' stage: 8.8 GW

facility GW by state (all dates)

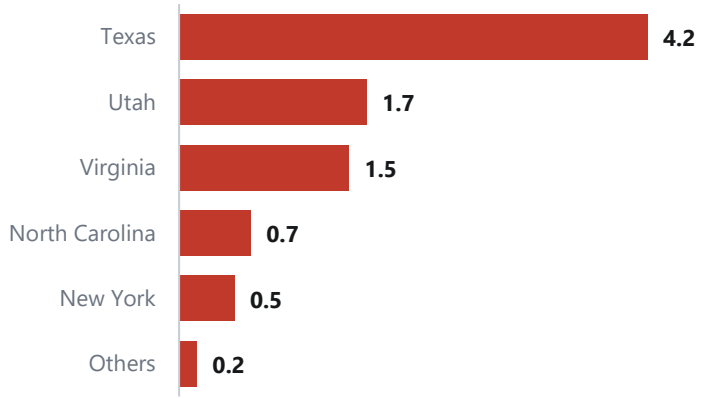

Who is delayed

- **Low likelihood: 6.0 GW**; high 2.0; medium 0.8. Mostly weak projects, not large builds stalled.
- Texas has 4.2 GW (48%) — before the TCEQ freeze (21-Sep) reached the data.

② Aterio's date vs the public date

pipeline with both dates: 77.8 GW

ATERIO LATER
33.2 GW
43% of comparable · >1 month


MEDIAN LAG
14 months
MW-weighted · 8.7 GW earlier

State	Both dates	Aterio later	%
Texas	25.4	14.8	58%
New York	7.2	2.1	30%
West Virginia	1.7	1.7	100%
Utah	1.6	1.6	100%
Georgia	6.2	1.5	24%
Virginia	5.4	1.4	27%
US	**77.8**	**33.2**	**43%**

Under construction: 11.1 of 22.7 GW with Aterio's date later.

③ Track record: Aug-25 construction

22.3 GW building on 31-Aug-25 · how far its date moved by 31-Aug-26

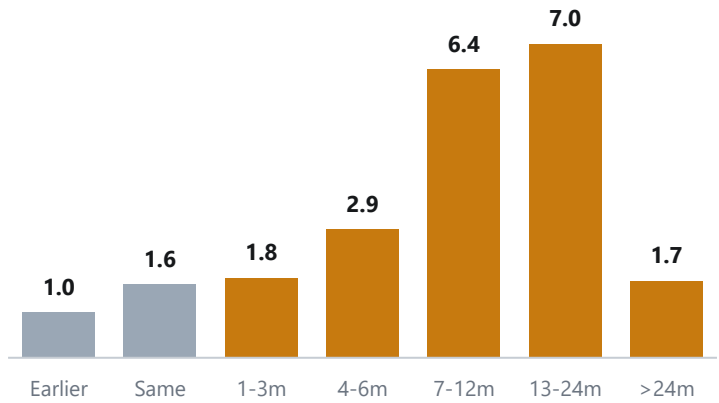

88% pushed out, median 9 months

- Of what was due by 31-Aug-26 (15.2 GW), **only 3.9 GW went live**; 9.8 GW is still building.
- Over 6 months (Feb-26 construction): 53% pushed out, median 2 months. Part of it is Aterio re-estimating its own dates.

Reading: what is flagged as delayed is small and low likelihood; the relevant delay is already inside Aterio's dates (14 months after the public source), and even so the track record shows construction slipping ~9 months a year. The data is as of 31-Aug: the post-election pauses are not in it yet.

Source: Aterio data-center census (inventory as of 31-Aug-26; weekly report with the 27-Aug-26 forecast) — licensed, internal use; Capstone calculations. **GW = facility power** (SELECTED_POWER_CAPACITY_MW), building level — not IT load (facility/IT ~1.15 in the same data) nor the campus-level cut of the reference deck (139.5 GW). Dates: the activation date Aterio publishes is its own estimate in 95% of buildings that carry both (only 39% match the public source), so slide 1 already carries this delay. Track record = buildings under construction in the 31-Aug-25 (and 28-Feb-26) inventory vs their date at 31-Aug-26.


3 · Aterio's scenarios — optimistic, baseline and conservative, by state

ATERIO

In Aterio's own forecast, 2026-30 runs from 346 GW (optimistic) to 210 GW (conservative); baseline 283 GW. The 136 GW gap sits almost entirely in 2028-30: 2026 is identical in all three and 2027 varies by 5.1 GW.

GW added per year, three scenarios

US · facility GW · sum 2026-30: 346 / 283 / 210

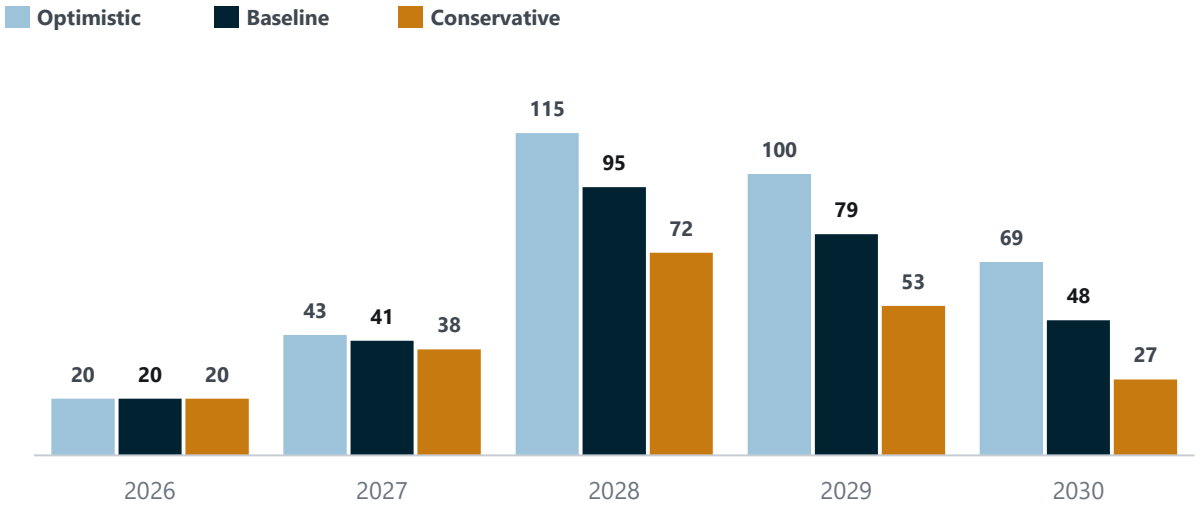

What each scenario contains (Capstone read)

• **Optimistic ≈ the whole live pipeline at stated dates** (2030 cumulative: 390 vs 397 GW rebuilt). **Conservative ≈ online + building + high likelihood** (254 vs 257). **Baseline sits between**, consistent with medium and low weighted near their stated probabilities.

Additions 2026-30 by state, by scenario

facility GW · ordered as in the inventory (slide 1)

State	Optim.	Base	Conserv.	Cons./Opt.
Texas	95.6	**77.4**	55.3	58%
Virginia	42.4	**37.3**	30.4	72%
Georgia	19.7	**16.2**	11.5	58%
Pennsylvania	17.9	**13.4**	8.4	**47%**
Ohio	16.1	**14.8**	12.9	80%
Utah	11.7	**8.4**	5.1	**44%**
Arizona	12.2	**9.7**	6.2	**51%**
Indiana	10.1	**9.3**	7.9	78%
New York	9.6	**5.4**	0.6	**7%**
Illinois	9.1	**7.0**	4.9	**54%**
Nevada	8.4	**7.8**	7.2	85%
West Virginia	7.4	**6.6**	5.4	74%
Other 32	86.0	**69.6**	54.0	63%
US	**346.3**	**282.9**	**209.9**	**61%**

Reading: the conservative case cuts 39% from the optimistic one. Texas goes from 96 to 55 GW; New York nearly vanishes (9.6 → 0.6 GW), because its pipeline is medium/low likelihood. The scenarios date from 27-Aug: they do not include the Texas pauses (TCEQ, 21-Sep) or the 3-Nov election.

Source: Aterio data-center census (inventory as of 31-Aug-26; weekly report with the 27-Aug-26 forecast) — licensed, internal use; Capstone calculations. **GW = facility power** (SELECTED_POWER_CAPACITY_MW), building level — not IT load (facility/IT ~1.15 in the same data) nor the campus-level cut of the reference deck (139.5 GW). Scenarios = cumulative activation forecast in the weekly report ('Evo State' sheet, 27-Aug-26); additions 2026-30 = cumulative 2030 − 2025. Aterio does not document the method; the composition read is Capstone's, rebuilding the scenarios from the inventory.
